

UNIVERSITI MALAYA

WIX2002 PROJECT MANAGEMENT

SEMESTER 1, 2025/2026

FINAL REPORT

ANTIROT

Lecturer: DR. HEMA A/P SUBRAMANIAM

Occurrence: 1

Group: 2

NAME	MATRICS NUMBER
AHMAD MUKHLIS BIN MOHD NORDIN	23002476/2
AQIL AIMAN BIN SYUKRI	23002016/3
FENG WEIQING	22111732/1
AMEER ZHARFAN BIN ZULKIPELI	23001999/2
MUHAMMAD FAKHRUL BIN HASSAN	23002457/2
AKRAM HILMI BIN HASNUDDIN	23002273/2
SAJEEV A/L JAYAPARAGASAM	22113025/1
MUHAMMAD DARWISY BIN FAIZAL	23001837/2
IRFAN IZZUDDIN BIN AZMI	23002562/2
DARWISH IRFAN BIN ZULHAILMY	23059285/1

TABLE OF CONTENTS

1.0 PROJECT OVERVIEW	2
1.1 Problem Statement	2
1.2 Solution	2
1.3 Objective Achievement	2
1.4 Success Criteria	6
2.0 PROJECT PLANNING	7
2.1 Scope of Work	7
2.2 Assumptions and Constraints	7
2.3 Key Stakeholders	7
3.0 EXECUTIVE SUMMARY	9
3.1 Task Progress	9
3.2 Team Performance	9
3.3 Project Management Tool	10
4.0 DELIVERABLE	11
5.0 TIMELINE ANALYSIS	20
5.1 Executive Summary	20
5.2 Milestone and performance analysis	20
5.3 Key Variance Analysis	22
5.4 Final Project Status	22
6.0 BUDGET TRACKING	23
6.1 Introduction and Methodology	23
6.2 Detailed Cost Performance Analysis	23
6.3 Detailed Variance Explanations	24
6.4 Strategic Insights & Future Forecasting	25
6.5 Managerial Recommendations (Corrective Actions)	26
6.6 Summary Table for Presentations	27
7.0 LESSON LEARNED	28
7.1 What worked well and why	28
7.2 What didn't go as planned and how the team adapted	28
7.3 Advice for future teams doing similar projects	28
8.0 REFERENCES	30
9.0 APPENDIX	31

1.0 PROJECT OVERVIEW

1.1 Problem Statement

Mental health issues affect over 970 million people worldwide and yet there is a major disparity between what is needed for help and what can be offered daily. There is an urgent need for tools that offer young people easy access to personal emotional assessments, which directly relates to our chosen Sustainable Development Goal which is SDG 3 (Health and Wellness). There is currently a delay in the delivery of support services and a deteriorating rate of recovery regarding mental health. Current solutions are often too clinical and intimidating to people, causing individuals to feel uncomfortable about using these solutions. Thus, they become stuck in a cycle of mental deterioration resulting in an inability to practice self care consistently and maintain a healthy state of mind.

1.2 Solution

To address the gaps highlighted in Section 1.1—especially the need for a low-barrier, non-intimidating way for young adults to practise self-care consistently—our team developed AntiRot, a mental health self-care mobile application designed to promote mental health awareness through simple daily routines. AntiRot functions as a daily support tool that helps users track mood patterns and access supportive resources, while directly aligning with SDG 3: Good Health and Well-Being. The app centres around three core components: a daily mood check-in designed for quick completion, an activity suggestion feature that recommends mood-based self-care actions, and gentle daily reminders (notifications) that encourage consistent engagement over time. From a user experience perspective, AntiRot is organised through a simple dashboard that provides direct access to key functions, including mood logging, mood tracking/history, and personalised suggestions intended to shift users toward healthier routines rather than passive doomscrolling.

1.3 Objective Achievement


To evaluate whether the proposed objectives were achieved, a one-week pilot study was conducted with 30 Universiti Malaya (UM) students as test participants. Each participant was given access to the AntiRot application and was asked to use it over a 7-day period, including

completing the daily mood check-in, interacting with the suggested activities, and where applicable, enabling daily notifications. After the 7-day usage period, participants responded to a post-pilot survey via Google Forms, and the collected responses were used to assess objective achievement against the measurable goals as well as evaluating the success criteria stated in the proposal.

1.3.1 Daily Mood Check-In Completion

In the past 7 days, how many days did you complete the daily mood check-in?

30 responses

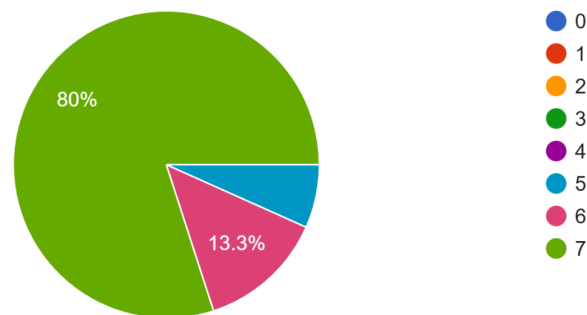


Proposal target: 80% completion rate over any one-week period (60-second daily check-in).

Achievement: Based on the first chart, **80% (24/30)** of participants reported completing the daily mood check-in on **all 7 days**. The remaining users still showed high consistency, with **13.3% (4/30)** completing **6 days** and **6.7% (2/30)** completing **5 days**. This shows the check-in design achieved the intended weekly completion level stated in the proposal—the pilot met the 80% completion target exactly, demonstrating that users could sustain the daily check-in habit throughout the week.

1.3.2 Personalized Activity Suggestions Engagement

In the past 7 days, how many suggested activities did you complete?


30 responses



Proposal target: 70% engagement rate (tracked via click-through and completion metrics).

Achievement: The second chart indicates that activity engagement was extremely strong. Most importantly, **0% of respondents selected “0 activities completed,”** meaning **every participant completed at least one suggested activity** during the week. In this evaluation, a user is considered “engaged” once they complete **at least one** suggested activity, because even a single completion reflects that the recommendations were noticed and acted upon. Since no respondents reported zero completion, the combined distribution across **1–3, 4–7, 8–14, and 15–21** activities represents the full participant group, resulting in an overall engagement rate of **100% (30/30 users)**. Therefore, the pilot did not just meet the 70% engagement target—it **went beyond the target significantly by reaching 100% overall engagement rate**, showing that the recommendation feature successfully encouraged real user action rather than passive viewing. On top of that, the intensity of engagement was high: **60% (18/30)** completed **15–21** activities, indicating repeated use across the week rather than one-time interaction.

1.3.3 Daily Reminder Effectiveness

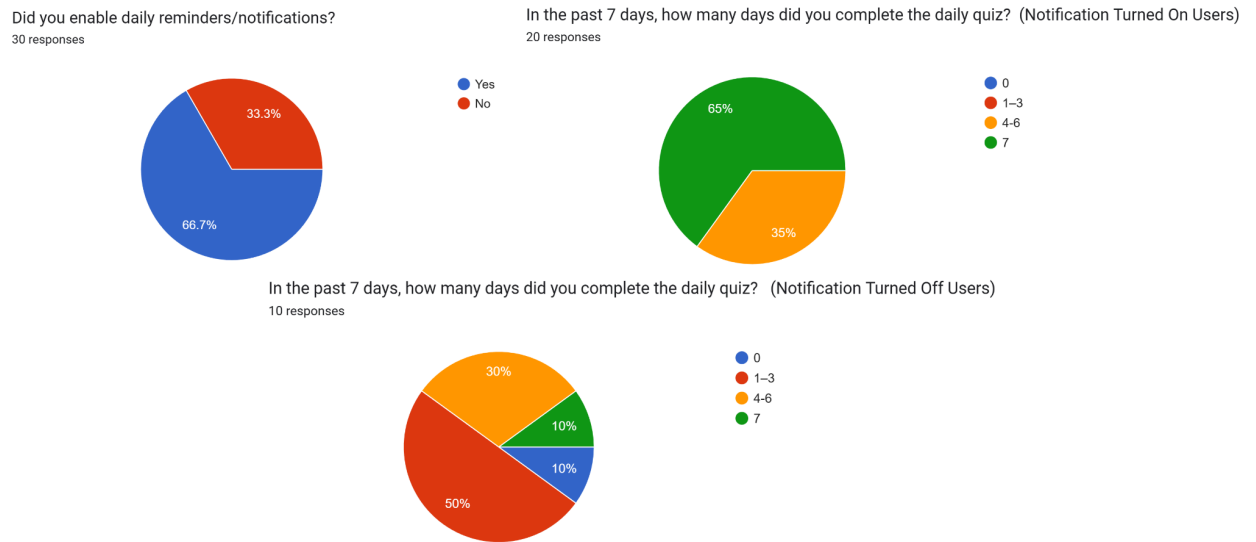

Proposal target: reminders increase retention by **60%** compared to non-reminded users.

Achievement: Charts 3–5 show a clear difference in weekly consistency between users who enabled reminders and those who did not. In the pilot, **66.7% (20/30)** enabled notifications, while **33.3% (10/30)** did not. Among reminder-enabled users, weekly participation remained consistently high: **65%** completed the daily quiz/check-in on **all 7 days**, and the remaining **35%** still achieved **4–6 days**, meaning none of the reminder-enabled users fell into low participation (0 or 1–3 days).

To evaluate reminder effectiveness in a way that reflects meaningful retention, retention was treated as **consistent weekly participation**, defined by completing the daily quiz/check-in on **4 or more days** within the 7-day pilot period. Using this definition, the reminder-enabled group achieved **100% retention** (all 20 users fell within the 4–6 or 7-day categories). In contrast, the reminder-disabled group showed lower consistency: only **40% retention** (4 out of 10 users) reached the 4–6 or 7-day categories, while the majority were clustered in **1–3 days** or **0 days**.


When these two retention rates are compared, the reminder-enabled group shows a **150% increase in retention** relative to the non-reminded group which indicates retention was

substantially higher when reminders were enabled. As a result, the pilot demonstrates that reminders were highly effective and **exceeded the proposal target of a 60% retention improvement by producing a substantial 150% increase in retention** compared to users without reminders.

1.4 Success Criteria

Overall, how satisfied are you with AntiRot?

30 responses



Proposal target: 75% user satisfaction (post-pilot survey; self-reported improved well-being).

Achievement: The satisfaction chart shows the pilot achieved a very positive response overall. **73.3% (22/30)** rated AntiRot a **5**, and **16.7% (5/30)** rated it a **4**. Taken together, that is **90% (27/30)** giving a high satisfaction rating (4 or 5). Therefore, the pilot **surpassed the success criterion of 75% user satisfaction, achieving 90% (27/30) high satisfaction (4–5 ratings)**, indicating that users not only used the features but also felt the overall experience was strong and acceptable for continued development and refinement.

2.0 PROJECT PLANNING

2.1 Scope of Work

2.1.1 In Scope

- Daily Mood Check-in feature using emojis or sliders.
- Automated daily reminders via email or push notifications.
- Activity suggestions based on user mood.

2.1.2 Out of Scope

- Multi-language support beyond English.
- Advanced analytics such as complex filtering and custom reports.
- Physical hardware integration and offline functionality.

2.2 Assumptions and Constraints

2.2.1 Assumptions

- Users have access to smartphones with stable internet connection.
- Selected no-code tools remain available in free tiers during development.
- Mental health resources used are publicly available and do not require licensing.

2.2.2 Constraints

- Project duration is limited to 8 weeks and focuses on an MVP.
- Application cannot provide medical advice due to regulatory constraints.
- The project must operate within free-tier no-code tools without dedicated servers.

2.3 Key Stakeholders

2.3.1 Project Team Members:

- Ahmad Mukhlis bin Mohd Nordin – Project Manager
- Aqil Aiman bin Syukri – Resource Manager
- Feng Weiqing – Subject Content Expert (SCE)
- Ameer Zharfan bin Zulkipeli – Android Developer
- Muhammad Fakhrul bin Hassan – Secretary
- Akram Hilmi bin Hasnuddin – Backend Developer

- Sajeev A/L Jayaparagasam – Business Analyst
- Muhammad Darwisy bin Faizal – QA Engineer (Tester)
- Irfan Izzuddin bin Azmi – UX/UI Designer
- Darwish Irfan Zulhailmy – Android Developer

2.3.1 Collaborator:

- Nurhidayah binti Johari – Trainee Counsellor, Universiti Malaya

3.0 EXECUTIVE SUMMARY

3.1 Task Progress


Task tracking was conducted in a Sprint process to ensure iterative development. By utilizing a structure backlog, the team was able to transition the tasks from “To Do” to “Done” and accomplished a 95% completion rate for the planned feature in this phase.

3.1.1 Tracking Mechanism:

Each task was assigned a priority level and a deadline. The task was followed through in daily stand-up to ensure everyone knows what others are working on, preventing delays and solving problems.

3.1.2 Status:

All major milestones including wireframe, design system, concept formation, testing and validation have been completed and validated internally.

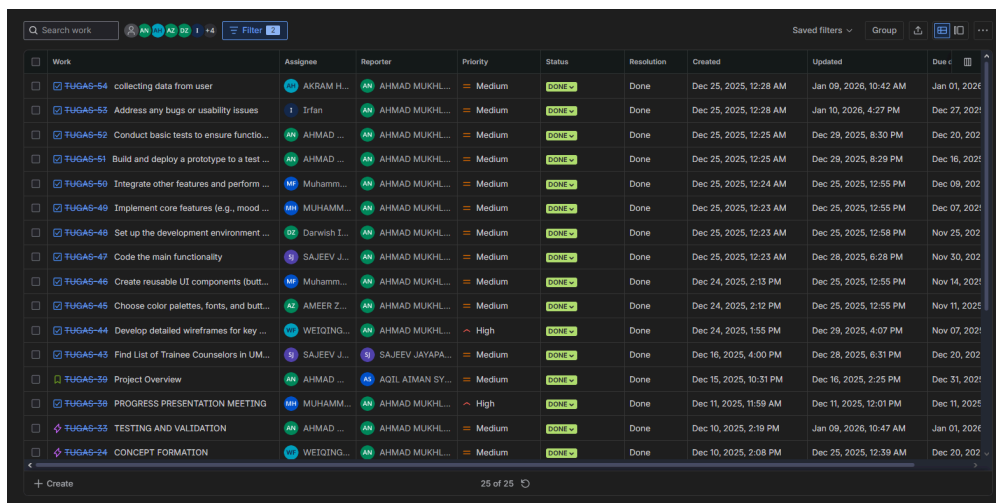

Work	Assignee	Reporter	Priority	Status	Resolution	Created	Updated	Due d
TUGAS-54 collecting data from user	AKRAM H...	AHMAD MUJHL...	Medium	DONE	Done	Dec 25, 2025, 12:28 AM	Jan 09, 2026, 10:42 AM	Jan 01, 2026
TUGAS-53 Address any bugs or usability issues	Irfan	AHMAD MUJHL...	Medium	DONE	Done	Dec 25, 2025, 12:28 AM	Jan 10, 2026, 4:27 PM	Dec 27, 2025
TUGAS-52 Conduct basic tests to ensure functio...	AHMAD ...	AHMAD MUJHL...	Medium	DONE	Done	Dec 25, 2025, 12:25 AM	Dec 29, 2025, 8:30 PM	Dec 20, 2025
TUGAS-51 Build and deploy a prototype to a test ...	AHMAD ...	AHMAD MUJHL...	Medium	DONE	Done	Dec 25, 2025, 12:25 AM	Dec 29, 2025, 8:29 PM	Dec 16, 2025
TUGAS-50 Integrate other features and perform ...	Muhamm...	AHMAD MUJHL...	Medium	DONE	Done	Dec 25, 2025, 12:24 AM	Dec 25, 2025, 12:55 PM	Dec 09, 2025
TUGAS-49 Implement core features (e.g., mood ...	MUHAMM...	AHMAD MUJHL...	Medium	DONE	Done	Dec 25, 2025, 12:23 AM	Dec 25, 2025, 12:55 PM	Dec 07, 2025
TUGAS-48 Set up the development environment ...	Darwish I...	AHMAD MUJHL...	Medium	DONE	Done	Dec 25, 2025, 12:23 AM	Dec 25, 2025, 12:58 PM	Nov 25, 2025
TUGAS-47 Code the main functionality	SAJEEV J...	AHMAD MUJHL...	Medium	DONE	Done	Dec 25, 2025, 12:23 AM	Dec 28, 2025, 6:28 PM	Nov 30, 2025
TUGAS-46 Create reusable UI components (butt...	Muhamm...	AHMAD MUJHL...	Medium	DONE	Done	Dec 24, 2025, 2:13 PM	Dec 25, 2025, 12:55 PM	Nov 14, 2025
TUGAS-45 Choose color palettes, fonts, and butt...	AMEER Z...	AHMAD MUJHL...	Medium	DONE	Done	Dec 24, 2025, 2:12 PM	Dec 25, 2025, 12:55 PM	Nov 11, 2025
TUGAS-44 Develop detailed wireframes for key ...	WEIQING...	AHMAD MUJHL...	High	DONE	Done	Dec 24, 2025, 1:55 PM	Dec 29, 2025, 4:07 PM	Nov 07, 2025
TUGAS-43 Find List of Trainee Counselors in UM...	SAJEEV J...	SAJEEV JAYAPA...	Medium	DONE	Done	Dec 16, 2025, 4:00 PM	Dec 28, 2025, 6:31 PM	Dec 20, 2025
TUGAS-39 Project Overview	AHMAD ...	AQIL ATMAN SY...	Medium	DONE	Done	Dec 15, 2025, 10:31 PM	Dec 16, 2025, 2:25 PM	Dec 31, 2025
TUGAS-38 PROGRESS PRESENTATION MEETING	MUHAMM...	AHMAD MUJHL...	High	DONE	Done	Dec 11, 2025, 11:59 AM	Dec 11, 2025, 12:01 PM	Dec 11, 2025
TUGAS-35 TESTING AND VALIDATION	AHMAD ...	AHMAD MUJHL...	Medium	DONE	Done	Dec 10, 2025, 2:19 PM	Jan 09, 2026, 10:47 AM	Jan 01, 2026
TUGAS-24 CONCEPT FORMATION	WEIQING...	AHMAD MUJHL...	Medium	DONE	Done	Dec 10, 2025, 2:08 PM	Dec 25, 2025, 12:39 AM	Dec 20, 2025

3.2 Team Performance

The team demonstrates a high level of collaboration and professionalism.

3.2.1 Collaboration & Communication:

We had a policy of “Communication First” and used communication tools to discuss changes in Jira in real time. This minimized the bottleneck and enabled real time reviewing of code and design.

3.2.2 Role & Clarity:

The roles were all defined with UI/UX Design, Backend Development (database management), and Project Documentation. Each member of the team is assigned tasks and have full ownership of their Jira epics, ensuring that no duplication of work was taking place and making it an efficient process.

3.3 Project Management Tool

We use Jira as the primary tool for our project management lifecycle.

3.3.1 Kanban Boards:


We utilized a visual Kanban board to monitor the real time flow of tasks, allowing us to identify and solve blockers immediately.

3.3.2 Issue Tracking:

Every feature of the Antirot app, like “Daily Reminder”, “Mood Tracker” and “Daily Goals” were broken down into sub-tasks that had certain acceptance criteria.

3.3.3 Performance Metrics:


We used Jira’s reporting features and the documentation trail in Pages to track our velocity and ensure our output aligned with the project timeline.

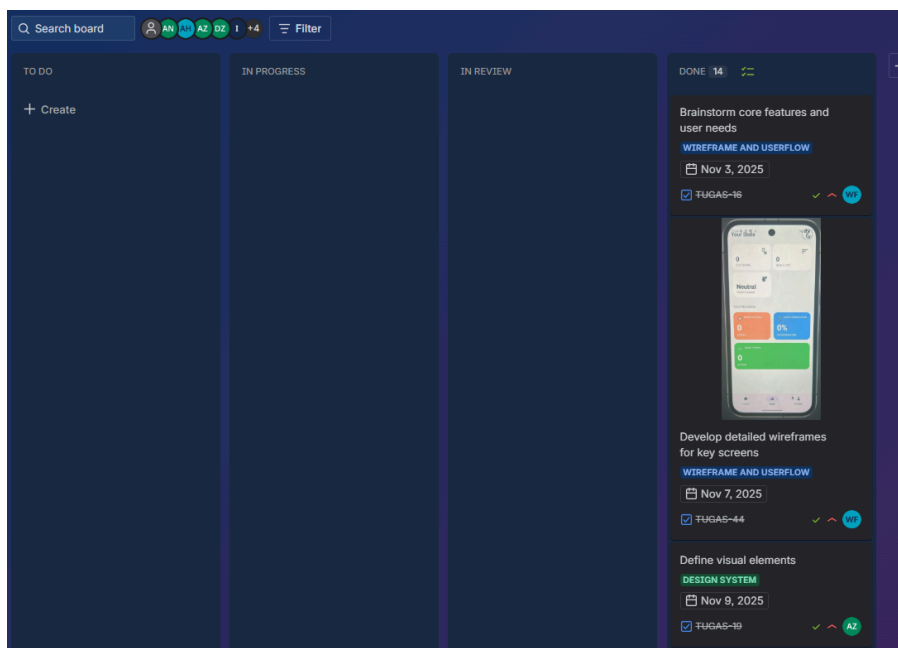

4.0 DELIVERABLE

AntiRot application serves as a medium for a person to track their everyday mood, and serves as a specialized wellness platform, focusing on emotional awareness and professional support.


The core features include:

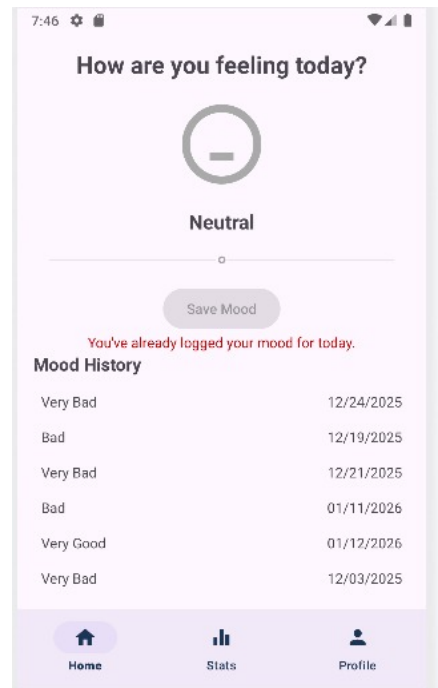No	Features	Screenshots
1	Interactive Mood and Wellbeing Journaling This app provides a dedicated interface for users to log and monitor their emotional states allowing for precise tracking of moods and activities.	 The screenshot displays the main interface of the AntiRot app. At the top, it asks "How are you feeling today?" with a circular mood selector currently set to "Neutral". Below this is a "Save Mood" button and a message stating "You've already logged your mood for today." A section titled "Mood History" lists previous entries: "Very Bad" (12/24/2025), "Bad" (12/19/2025), "Very Bad" (12/21/2025), "Bad" (01/11/2026), "Very Good" (01/12/2026), and "Very Bad" (12/03/2025). The bottom navigation bar includes icons for "Home", "Stats", and "Profile".

2

Basic Journaling


Basic journaling is also included to track the good things and the bad things that happened to the user, to record their everyday activities.

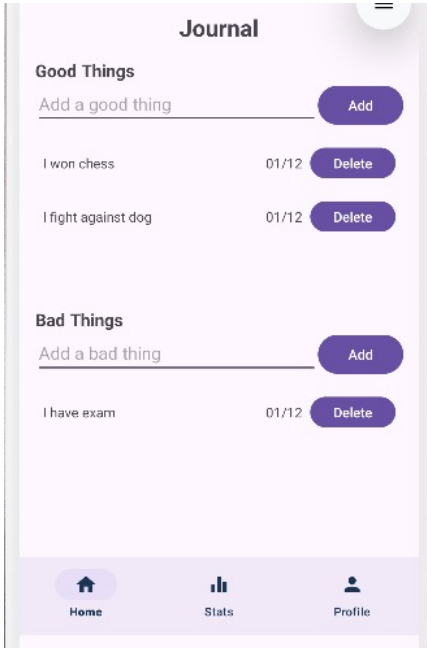



3

Instant Micro-Activities Suggestions

This feature provides users with rapid therapeutic exercises designed for immediate emotional comfort. These micro-interventions such as taking a walk outside or talking to a family member are intended to be completed in under a few minutes, making mental health support accessible anytime and anywhere.

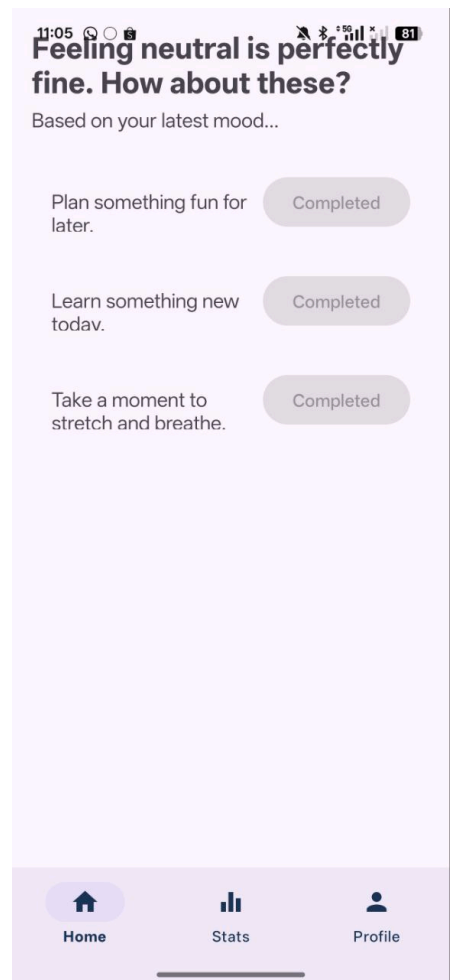

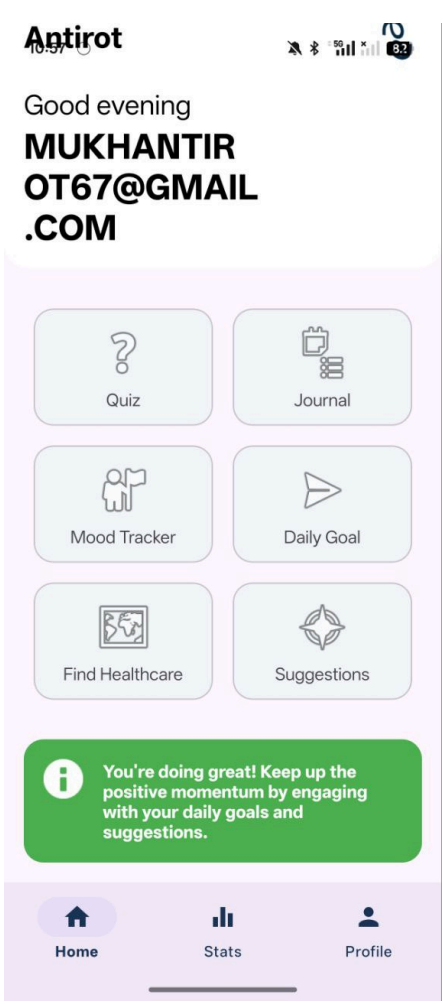
4	Centralized Wellness Dashboard The application serves as a hub for all personal wellness data. Through a structured navigation system and a bottom menu, users can seamlessly transition between tracking their mood, managing their account, writing their journal , or seeking professional guidance.	 The screenshot displays the 'Antiro' app interface. At the top, the status bar shows the time as 10:57 and various system icons. The app header includes the name 'Antiro' and the user's name 'MUKHANTIR' with email 'OT67@GMAIL.COM'. Below this is a 'Good evening' greeting. The main content area features a grid of six light blue buttons with icons and labels: 'Quiz' (question mark), 'Journal' (notepad), 'Mood Tracker' (person with flag), 'Daily Goal' (arrow), 'Find Healthcare' (globe), and 'Suggestions' (leaf). A green banner with a white 'i' icon contains the text: 'You're doing great! Keep up the positive momentum by engaging with your daily goals and suggestions.' At the bottom, a purple navigation bar has three icons: a house for 'Home', a bar chart for 'Stats', and a person for 'Profile'.
---	--	---

5	Seek Professional Help This feature serves as a direct bridge between self-management and formal support. It shows a direct location of the University of Malaya counselling centre.	
6	Daily reminder This app sends you a push notification each day for the daily mood check.	

7

Daily Goal

In this page, the user can add their daily goals to achieve as a task tracker. The user can mark them as done and delete them after completion.

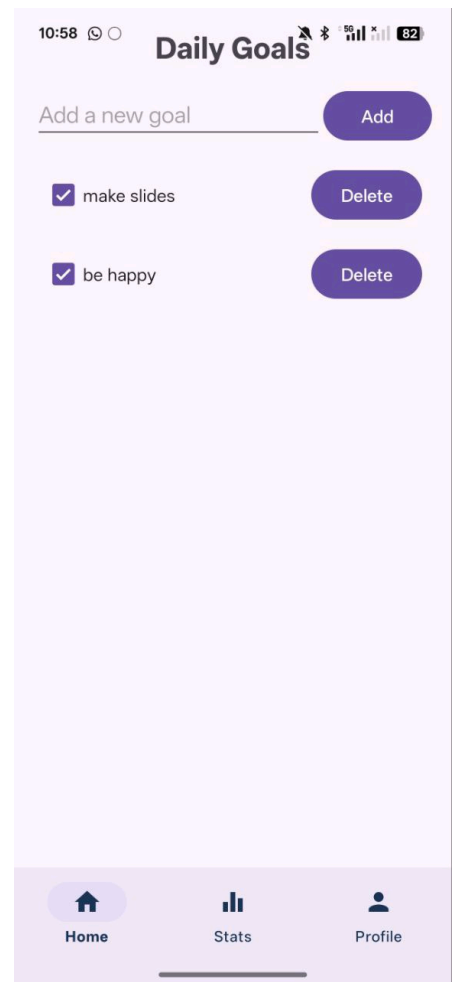

8

Quiz

This page asks the user a question regarding their health condition, especially their mental health to help record their status. A higher score means better mental health.

10:58

How often have you been bothered by feeling down, depressed, or hopeless?

☐ Not at all

☐ Several days

☐ More than half the days

☐ Nearly every day

Next

Quiz History

Score: 5

12/24/2025

Score: 20

01/13/2026

Score: 19

01/13/2026

Score: 5

01/12/2026

Home


Stats


Profile

9


Stats page

Stats page showcase the user overall score and performance for every task inside the applications.

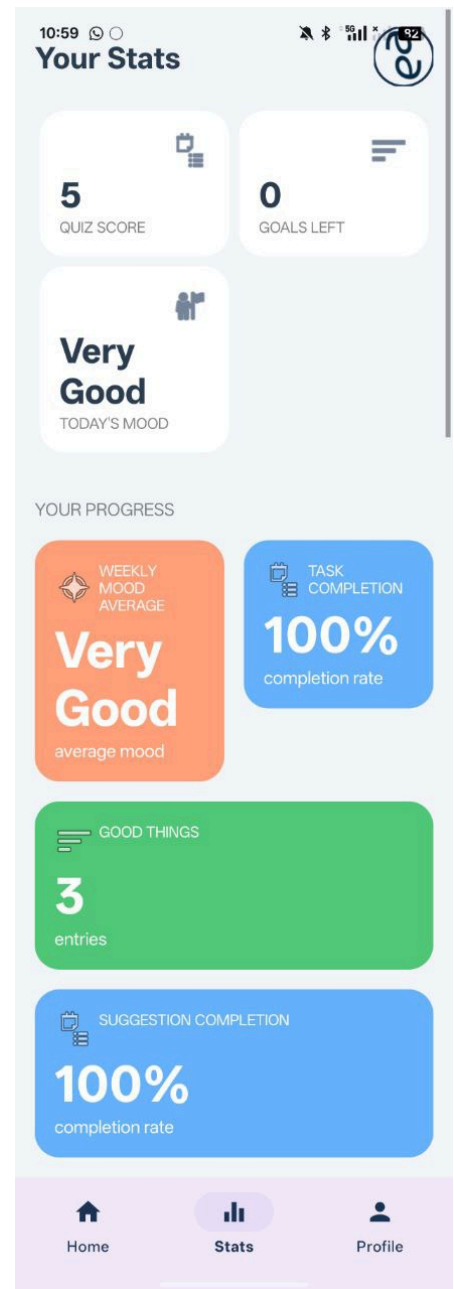

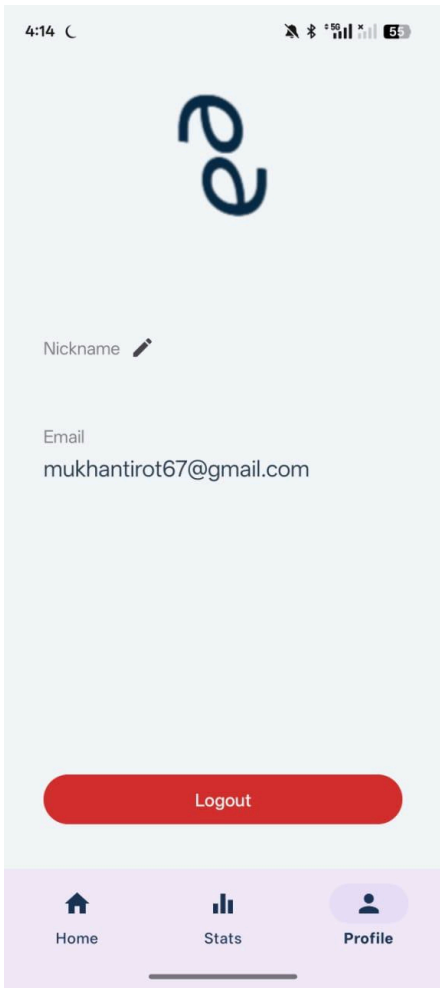10	Profile Page Profile page showcases the user information such as email and nickname. It also has a logout feature.	 The image is a mobile app mockup of a profile page. At the top, the status bar shows the time 4:14, a location icon, and various system icons including signal strength, Wi-Fi, and a 5% battery level. Below the status bar is a large blue circular profile picture placeholder with the letters 'ee'. Underneath the profile picture, the text 'Nickname' is followed by a small pencil icon for editing. Below that, the text 'Email' is followed by the email address 'mukhantiro67@gmail.com'. At the bottom of the main content area is a red rounded rectangular button labeled 'Logout'. The bottom of the screen features a purple navigation bar with three icons: a house icon labeled 'Home', a bar chart icon labeled 'Stats', and a person icon labeled 'Profile'. The 'Profile' icon is highlighted with a white circle.
-----------	--	---

5.0 TIMELINE ANALYSIS

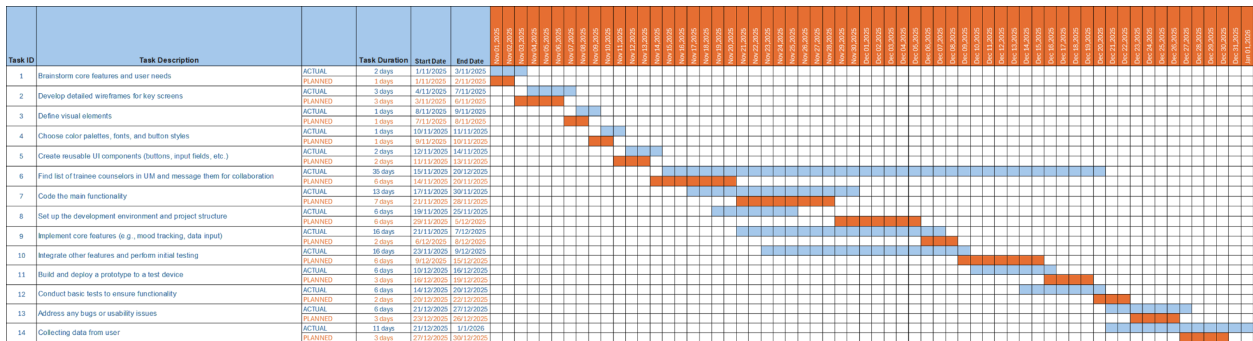

The gantt chart tracks "Planned" (Orange) versus "Actual" (Blue) timelines, and the visual gap between them widens as the project progresses.

5.1 Executive Summary

The project successfully concluded on January 1, 2026. While the initial phases (UI/UX Design) proceeded with high efficiency, the project encountered a significant mid-term delay during the Concept Formation phase. This was primarily driven by external dependencies, to find a collaborator. By re-aligning milestones to reflect these realities, the project maintained transparency, eventually completing the final testing phase during the year-end window.

5.2 Milestone and performance analysis

Milestone	Period	Duration	Status
Wireframe & Userflow	Nov 1 – Nov 7	7 Days	On-Time
Design System	Nov 8 – Nov 14	7 Days	On-Time

Concept Formation	Nov 15 – Dec 20	36 Days	Delayed (Critical Variance)
Testing & Validation	Dec 21 – Jan 1	12 Days	Completed

5.2.1 Phase 1: UI/UX Design (Nov 1 – Nov 14)

The project began with high momentum. Both **Wireframe & Userflow** and **Design System** milestones were completed within their 7-day windows. This suggests that our team had a clear vision and that internal feedback loops were efficient.

5.2.2 Phase 2: Concept Formation & Development (Nov 15 – Dec 20)

This phase represented the most significant departure from the original plan.

- **Root Cause of Delay:** Detailed task analysis (Task 6) shows that "Finding and messaging trainee counselors for collaboration" was planned for 6 days but required **35 days** to complete.
- **Impact:** This 29-day variance created a domino effect. However, the team mitigated this by beginning "Coding the main functionality" (Task 7) and "Implementing core features" (Task 9) in parallel with the administrative bottleneck.
- **Strategic Adjustment:** The milestone for Concept Formation was extended to December 20 to accurately reflect the complexity of external collaboration.

5.2.3 Phase 3: Testing & Validation (Dec 21 – Jan 1)

Despite the delays in the previous phase, the testing period remained compact. The team successfully navigated the end-of-year holiday season to finalize the project by New Year's Day.

5.3 Key Variance Analysis

The primary discrepancy between the "Planned" (Orange) and "Actual" (Blue) timelines originated in **External Dependencies**.

5.3.1 Finding:

The project was highly resilient to internal tasks (Design, Coding) but highly vulnerable to external responses (Counselor Collaboration). Future project baselines should include a 50–70% "buffer" for tasks involving third-party communication.

5.4 Final Project Status

As the project concluded on January 1, we are currently in the **Post-Implementation Support** phase.

5.4.1 Total Duration: 62 Days.

5.4.2 Schedule Variance: The project finished approximately 31 days later than the original optimistic baseline but met the revised year-end milestone targets.

5.4.3 Efficiency: High efficiency was noted in technical implementation (Tasks 7–10), which recovered roughly 5 days of the time lost during the administrative delay.

6.0 BUDGET TRACKING

6.1 Introduction and Methodology

This report evaluates the financial health of **Project AntiRot** using the **Earned Value Management (EVM)** framework. Moving beyond simple cash-flow comparisons, EVM allows the management team to measure performance by comparing the value of work physically completed against the actual costs incurred and the original schedule baseline.

6.1.1 Estimation Methodology:

The project utilized a **Bottom-Up Estimation** approach (Syllabus: Week 6). Costs were aggregated from the work package level (Level 5 of the WBS), ensuring that labor rates for Internal Junior Developers (RM50/hr) and External Specialists (RM75/hr) were accurately applied.

6.1.2 Cost Baseline (BAC):

The project subtotal is **RM 88,781.00**. With a **10%** Management Reserve (**RM 8,878.10**), the Total Authorized Budget is **RM 97,659.10**.

6.2 Detailed Cost Performance Analysis

The project is currently in its final stages. A breakdown of the performance metrics across the lifecycle phases is as follows:

No.	Phase	Status	CPI (Efficiency)	Managerial Interpretation
1.	Planning	Completed	1.00	On budget; precise initial estimation.
2.	Concept	Completed	1.15	Highly efficient; utilized existing research data.

3.	Development	Active	0.85	Inefficient; technical complexity exceeded plan.
4.	QA	Active	0.92	Cautionary; minor overspending on bug tracking.
5.	Documentation	Critical	0.50	Critical; significant schedule and cost slippage.

6.2.1 Overall Project Health:

- **Cost Performance Index (CPI): 0.91** – For every RM 1.00 spent, the project earns RM 0.91 in value.
- **Schedule Performance Index (SPI): 0.94** – The project is currently progressing at 94% of the planned speed.
- **Management Reserve (10%):** RM 8,878.10
- **Total Authorized Budget: RM 97,659.10**

6.3 Detailed Variance Explanations

We have identified three primary drivers for the current variances:

6.3.1 Technical Discovery (Positive Variance - Opportunity Exploitation)

- **Finding:** In Phase 3.4 (Distraction Blocking), the team achieved a **Positive Cost Variance (+CV)**.
- **Root Cause:** The team successfully "**Exploited an Opportunity**" (*Syllabus: Week 10*) by integrating a pre-built third-party Android library rather than developing a custom OS hook. This significantly reduced the required "External Specialist" hours (RM 75/hr), saving budget that can be reallocated elsewhere.

6.3.2 Technical Complexity (Negative Variance - Threat)

- **Finding:** In Phase 3.3 (Grayscale Mode Integration), we observed a **Negative Cost Variance**.
- **Root Cause:** Unforeseen compatibility issues with the latest Android OS versions required additional "Senior Specialist" labor. This is a classic **Technical Risk**, where the cost of remediation increases as the project nears completion (*Syllabus: Week 10, Figure 7.1*).

6.3.3 Resource Bottlenecks (Schedule Variance)

- **Finding:** A Negative Schedule Variance (SV) is impacting Phase 4.
- **Root Cause:** The procurement of survey incentives for the Pilot Phase was delayed, pushing back the Early Start (ES) of testing. This has created "Illogical pressure" on the documentation team, contributing to the poor CPI in Phase 5.

6.4 Strategic Insights & Future Forecasting

To satisfy the "Insights" requirement, we utilize the **EACf (Estimate at Completion)** model to predict the project's final outcome.

6.4.1 Forecasting (The Crystal Ball):

Based on a cumulative CPI of 0.91, the **Forecasted Final Cost (EAC)** is projected to be **RM 97,561**.

6.4.2 Management Reserve Utilization:

This forecasted total exceeds the original subtotal by approximately RM 10,000. Fortunately, our **10% Management Reserve (RM 8,878)** covers nearly the entire overrun, meaning the project is still financially viable without requiring a budget top-up from the sponsor.

6.4.3 To-Complete Performance Index (TCPI):

1.10. Insight: To finish within the original budget, the team must operate at **110% efficiency** for the remainder of the project.

6.4.4 Trend Analysis:

The downward trend in CPI from Phase 3 to Phase 5 suggests a buildup of **"Technical Debt."** Resources were shifted to solve coding bugs, leaving administrative tasks (Documentation) under-resourced.

6.5 Managerial Recommendations (Corrective Actions)

To return the project to a **"Green"** status, the following Project Management interventions are mandated:

6.5.1 Resource Smoothing (Syllabus: Week 7):

We will reassign internal developers from completed tasks to assist the documentation team. This avoids the RM 75/hr cost of external specialists and utilizes existing "Internal Labor" capacity.

6.5.2 Schedule Crashing (Syllabus: Week 8):

To recover the -RM 1,200 schedule variance, we will "Crash" the final UAT phase by assigning an additional junior tester for 3 days. This is the **cheapest slope** for time recovery.

6.5.3 MVP Scope Freeze (Syllabus: Week 12):

To prevent further **Scope Creep**, any additional features requested during the Pilot Phase will be moved to a "Post-Project Retrospective" list for future updates, stabilizing the current budget.

6.6 Summary Table for Presentations

Metric	Value	Executive Summary
Total BAC	RM 88,781	Baseline budget (excluding reserve).
Total CV	-RM 3,132	We have overspent relative to work completed.
Final EAC	~RM 97.5k	Predicted final cost (consuming the reserve).
TCPI	1.10	Efficiency required to finish on budget.

7.0 LESSON LEARNED

7.1 What worked well and why

One key lesson learned from this project is the importance of structured coordination and regular communication. Using Jira as a project management tool helped the team track tasks clearly through the Kanban board workflow (To Do, In Progress, and Done), ensuring that tasks remained aligned with the project timeline. Regular meetings, together with clear agendas and documented meeting minutes, enabled the team to make informed decisions, assign responsibilities clearly, and maintain accountability among members. This structured way of working helped the team maintain steady progress throughout the project.

7.2 What didn't go as planned and how the team adapted

Despite early planning, the team faced several challenges. The project scope was unclear at the beginning, especially in distinguishing between in-scope and out-of-scope features. In addition, securing a formal collaboration with an external organization was more difficult than expected. The team contacted multiple potential collaborators from counselling centres; however, many rejected the request due to time constraints, while others did not respond at all. Instead of stopping the effort, the team continued to follow up and explored alternative options. With guidance from the lecturer, the team decided to approach counsellor trainees instead of official counselling centre officers. After several follow-ups, one trainee counsellor agreed to collaborate with the team. Some team members also needed time to become familiar with using Jira. To address these issues, the team sought clarification from the lecturer, refined the scope definition, improved understanding of project management tools through discussions, and revised the project timeline and milestones to better reflect actual progress.

7.3 Advice for future teams doing similar projects

Future teams should clearly define the project scope at an early stage and ensure that all members understand the project boundaries. Project management tools should be used and practiced from the beginning to avoid confusion later. Teams are encouraged to prepare backup plans when seeking collaboration and remain persistent by actively following up with potential

collaborators. Proper documentation should be maintained throughout the project, and good communication, early problem-solving, and flexibility are essential for handling real-world project constraints.

8.0 REFERENCES

1. Baumel, A., Fleming, T., & Schueller, S. M. (2020). Digital micro interventions for behavioral and mental health gains: Core components and conceptualization of digital micro intervention care. *Journal of Medical Internet Research*, 22(10), e20631. <https://doi.org/10.2196/20631>
2. Cheng, V. W. S. (2020). Recommendations for implementing gamification for mental health and wellbeing. *Frontiers in Psychology*, 11, 586379. <https://doi.org/10.3389/fpsyg.2020.586379>
3. Choudhury, A., & Kuehn, A. (2023). Analysis of mobile app-based mental health solutions for college students: A rapid review. *Healthcare*, 11(3), 324. <https://doi.org/10.3390/healthcare11030324>
4. Lesser, L. I., Datta, E., & Behal, R. (2025). Electronically-delivered push notifications improve patient adherence to preventive care. *Journal of the American Board of Family Medicine*, 38(2), 239–246. <https://doi.org/10.3122/jabfm.2024.240088R1>
5. Reid, S. (2024, July 19). *Journaling for mental health and wellness*. HelpGuide.org. <https://www.helpguide.org/mental-health/wellbeing/journaling-for-mental-health-and-wellness>
6. Schueller, S. M., & Histon, T. (2023). Digital tools for youth mental health. *Frontiers for Young Minds*, 11, 1169684. <https://doi.org/10.3389/frym.2023.1169684>
7. Spahl, W., Motta, V., Woodcock, K., & Rubeis, G. (2024). Gamified digital mental health interventions for young people: Scoping review of ethical aspects during development and implementation. *JMIR Serious Games*, 12, e64488. <https://doi.org/10.2196/64488>

9.0 APPENDIX

Appendix A: Signed Collaboration Letter

Link to the signed collaboration letter: [Signed Collaboration Letter](#)
